



City of Omaha  
Public Works Dept.  
1819 Farnam St.  
Omaha, NE 68183  
cityofomaha.org  
402-444-5220

May 8, 2020

**Subject:** Construction Update – Jones Street between 11<sup>th</sup> and 13<sup>th</sup> Streets

Due to unexpected delays in relocation of utilities and completing service connections of those utilities, construction on the City of Omaha’s Jones Street project between 11<sup>th</sup> and 13<sup>th</sup> Streets has been **rescheduled to begin Thursday, May 14<sup>th</sup>**. In order to expedite construction along Jones Street, the phasing of construction has been revised as indicated on the enclosed map for your reference. Barring any weather delays or additional utility relocations, construction of the street project is anticipated to take place over the 2020 construction season; however, construction along 12<sup>th</sup> Street from Jones to Jackson Street may extend into the 2021 construction season.

Here is an overview of anticipated construction activities and an updated, expedited construction schedule for 2020:

Phase 1

- Thursday, May 14<sup>th</sup> – Closure of the intersection of 11<sup>th</sup> and Jones Street for removals and reconstructing the 11<sup>th</sup> Street intersection.
- May thru July – Construct storm sewer and roadway along Jones Street from 11<sup>th</sup> Street west to 13<sup>th</sup> Street. The 12<sup>th</sup> Street intersection will remain open to north/south traffic.

**\*\*Note:** *Jones Street from 11<sup>th</sup> to 12<sup>th</sup> Streets and from west of 12<sup>th</sup> to 13<sup>th</sup> Street will remain closed during Phase 1 construction.*

Phase 2

- Late July/Early August – Closure of the intersection of 12<sup>th</sup> and Jones Street for removals and reconstructing the 12<sup>th</sup> Street intersection. The 11<sup>th</sup> Street intersection will reopen to north/south traffic at this time.
- August to November – Construction of 12<sup>th</sup> Street from Jones to Jackson Street pending completion of Jones Street from 11<sup>th</sup> to 13<sup>th</sup> Street.

**\*\*Note:** *Pedestrian access to properties will be maintained at all times by designated routes with the construction of sidewalks and underground vault work phased accordingly during all phases of construction.*

Please keep in mind this schedule and operations are subject to change based on weather conditions. Temporary roadway, sidewalk, and parking stall closures will be in place as needed for the safety of the crews and public. The project team will keep all stakeholders updated as the project progresses. The project contractor, RPL Utility, will be providing regular notifications to and coordinating with all stakeholders prior to any change in vehicular or pedestrian access throughout the construction of the project.

For immediate, on-site assistance during construction, contact:


Travis Lienemann  
RPL Utility  
(402) 699-2843

Additionally, the following personnel are available to address questions and concerns throughout construction:

Alyssa Tenorio  
Construction Public Coordinator  
(402) 964-3965

Jon Mooberry  
Construction Project Manager  
(402) 443-7487

For more information and status updates regarding the project, please visit or sign up for project notifications at [www.keepomahamoving.com/projects](http://www.keepomahamoving.com/projects). Thank you for your patience during the construction of this project!

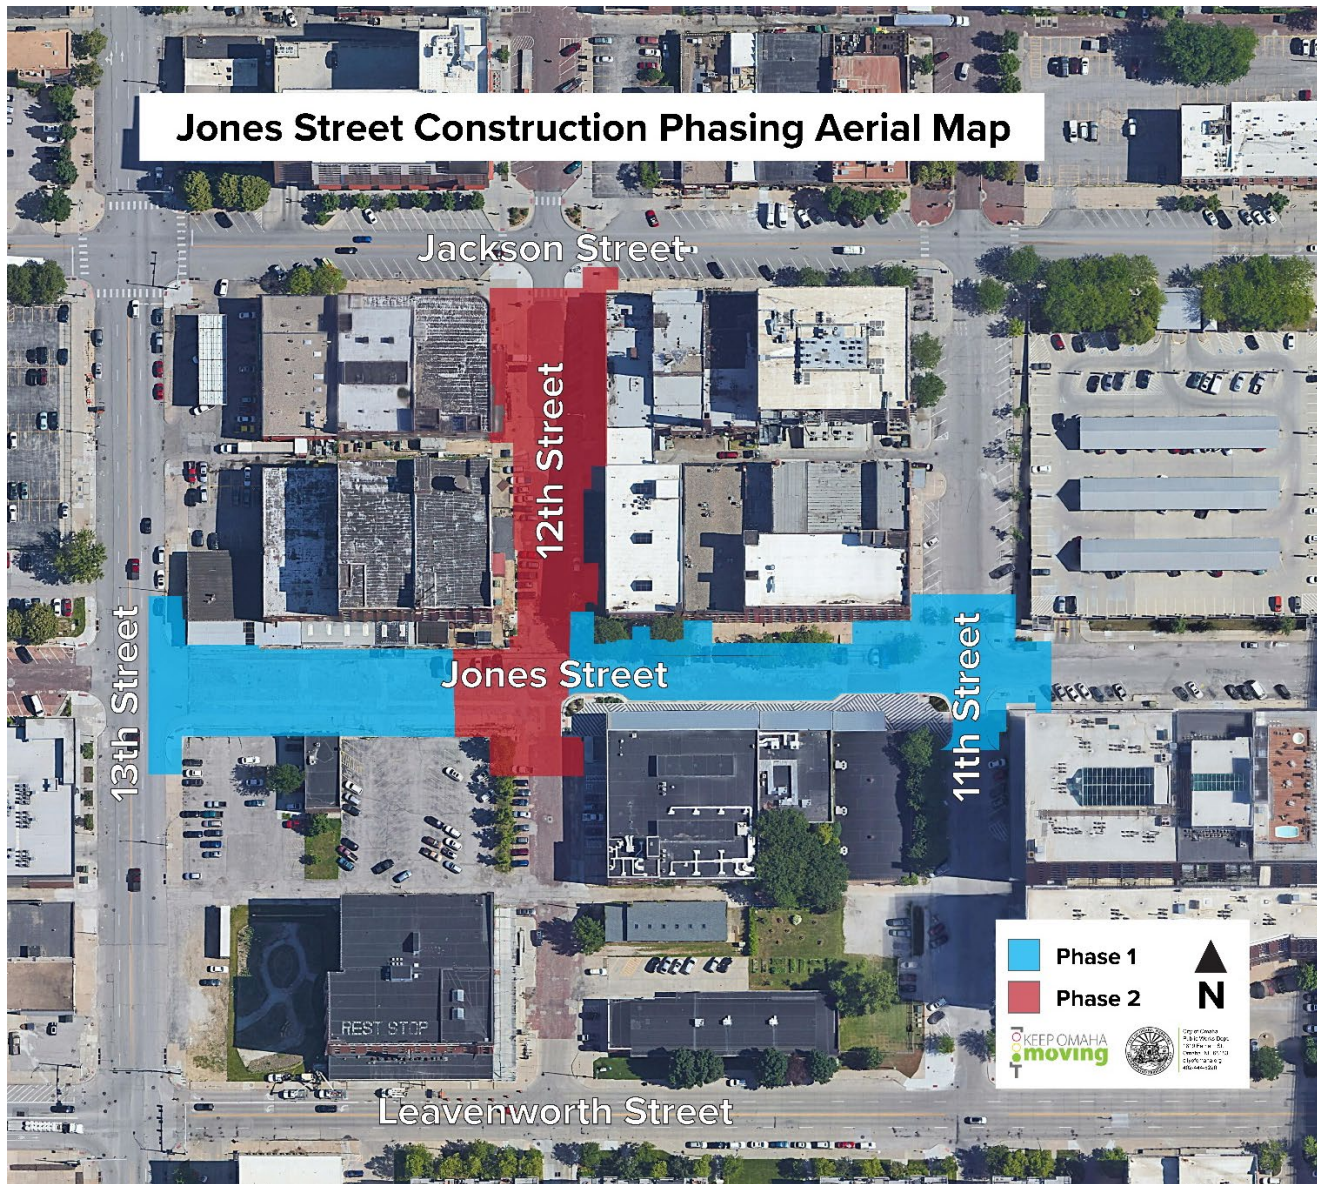

**LEGEND:**

**Phase 1 – Spring through Summer 2020**

**Phase 2 – Late Summer through Fall 2020**

*\*Construction of 12<sup>th</sup> Street under Phase 2 is dependent on weather and may possibly take place in 2021.*
